


ID		% Complet	Task Name	Current Projected Schedule Start Date	Current Projected Schedule Finish Date	Actual Start	Actual Finish	Baseline Schedule Start Date	Baseline Schedule Finish Date	Predecessor													
											2014				2015				2016				
											Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct
0		52%	10777G SouthSide School_17-Apr-2014	Tue 1/28/14	Thu 6/9/16	Tue 1/28/14	NA	Tue 1/28/14	Thu 6/9/16														
1	✓	100%	Preliminary Layout Approval by Commission	Tue 1/28/14	Tue 2/4/14	Tue 1/28/14	Tue 2/4/14	Tue 1/28/14	Tue 2/4/14														
2	✓	100%	DD Drawings [30%] to be Completed and Approved by Commission	Tue 2/4/14	Thu 4/17/14	Tue 2/4/14	Thu 4/17/14	Tue 2/4/14	Thu 4/17/14														
11	❗	75%	Agencies Approval	Fri 4/4/14	Fri 1/30/15	Fri 4/4/14	NA	Fri 4/18/14	Tue 6/17/14														
12	✓	100%	Prepare Documentation for Submittal FCT	Mon 1/5/15	Fri 1/30/15	Mon 1/5/15	Mon 2/16/15	Fri 4/18/14	Fri 5/2/14	16													
13	✓	100%	Prepare Documentation for Submittal Broward County Historic Society Presentation	Fri 4/4/14	Tue 11/4/14	Fri 4/4/14	Tue 11/4/14	Fri 4/18/14	Fri 5/2/14														
14	✓	100%	Prepare Documentation for Submittal Division of Cultural Affairs	Mon 1/5/15	Fri 1/30/15	Mon 1/5/15	Mon 2/16/15	Fri 4/18/14	Fri 5/2/14	16													
15		0%	Approval or Comments returned from FCT	Fri 1/30/15	Fri 2/13/15	NA	NA	Mon 5/5/14	Tue 6/17/14	16													
16	✓	100%	Approval or Comments returned from Broward County Historic Society	Mon 1/5/15	Fri 1/30/15	Mon 1/5/15	Fri 1/30/15	Mon 5/5/14	Tue 6/17/14	13FS+30 days													
17		0%	Approval or Comments returned from Division of Cultural Affairs	Thu 1/30/14	Fri 2/13/15	NA	NA	Mon 5/5/14	Tue 6/17/14	16													
18	✓	100%	CCNA RFQ execution for design consultants (under one umbrella)	Mon 3/3/14	Tue 10/21/14	Mon 3/3/14	Tue 10/21/14	Mon 3/3/14	Wed 8/20/14														
32		65%	Design & Permit Phase	Tue 4/1/14	Tue 3/31/15	Tue 4/1/14	NA	Tue 4/1/14	Mon 3/30/15														
33	✓	100%	Community Outreach (All Comments from Neighborhood Due)	Tue 4/1/14	Fri 5/30/14	Tue 4/1/14	Fri 5/30/14	Tue 4/1/14	Fri 5/30/14	10													
34	✓	100%	Review & Approval of 60% Design Development	Wed 10/22/14	Fri 1/9/15	Wed 10/22/14	Fri 1/9/15	Thu 8/21/14	Wed 10/1/14	31													
35	✓	100%	Review & Approval of 100% Design Development	Mon 1/12/15	Mon 1/26/15	Mon 1/12/15	Mon 1/26/15	Thu 10/2/14	Wed 11/12/14	34													
36	✓	100%	Design Development Complete	Mon 1/26/15	Mon 1/26/15	Mon 1/26/15	Mon 1/26/15	Wed 11/12/14	Wed 11/12/14	33,11,35													
37	✓	100%	Preliminary Cost Estimate	Wed 12/10/14	Wed 12/10/14	Wed 12/10/14	Wed 12/10/14	Thu 11/13/14	Wed 12/3/14	35													
38	✓	100%	Approval of 100% Design Development Drawings	Mon 1/26/15	Fri 1/30/15	Mon 1/26/15	Fri 1/30/15	Thu 12/4/14	Wed 12/17/14	37,35													
39		20%	Construction Documents	Fri 1/30/15	Fri 3/20/15	Fri 1/30/15	NA	Thu 12/18/14	Mon 2/2/15	38,14,17													
40		0%	Final Construction Estimate	Fri 3/20/15	Fri 3/27/15	NA	NA	Tue 2/3/15	Mon 2/16/15	39													
41		0%	Permitting	Fri 2/27/15	Fri 3/27/15	NA	NA	Tue 2/17/15	Mon 3/30/15	40													
42		0%	Bidding & Construction Phase	Tue 3/31/15	Thu 6/9/16	NA	NA	Tue 3/31/15	Thu 6/9/16														
43		0%	Bidding Process	Tue 3/31/15	Thu 4/30/15	NA	NA	Tue 3/31/15	Thu 4/30/15	41													
44		0%	Contract Award	Fri 5/1/15	Thu 6/11/15	NA	NA	Fri 5/1/15	Thu 6/11/15	43													
45		0%	Comission Approval	Fri 5/1/15	Thu 6/11/15	NA	NA	Fri 5/1/15	Thu 6/11/15	44SS													
46		0%	Construction Phase	Fri 6/12/15	Thu 6/9/16	NA	NA	Fri 6/12/15	Thu 6/9/16	45													

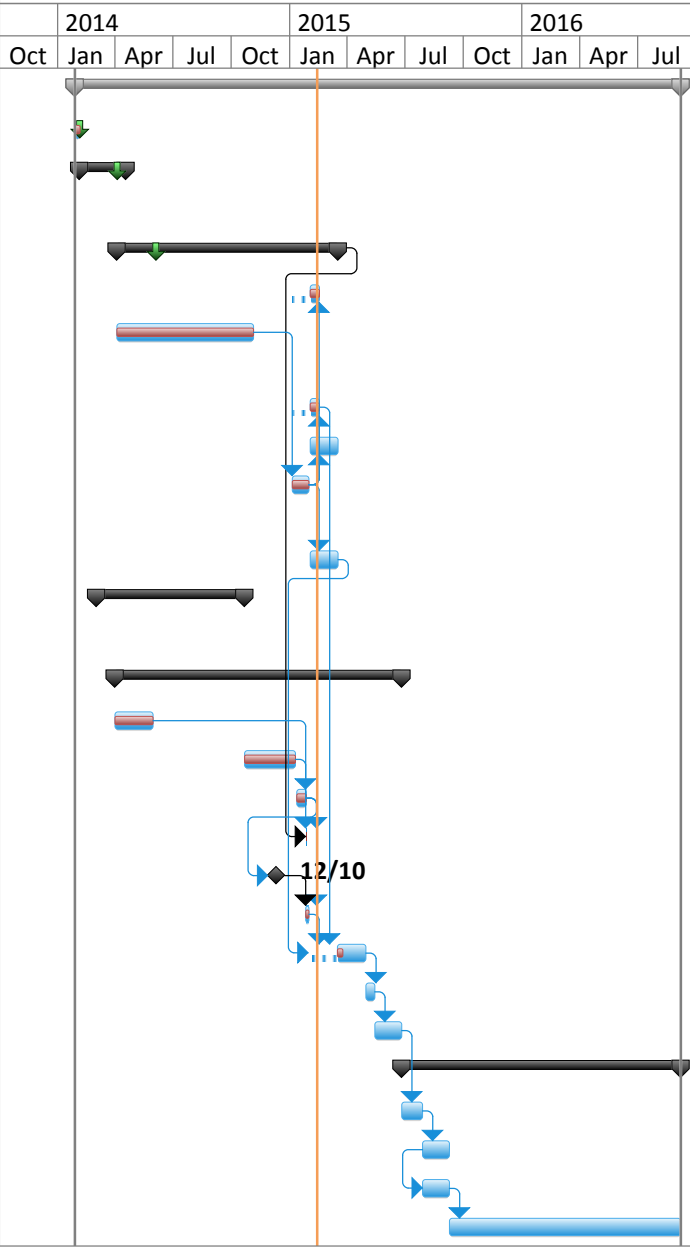

Project: 10777G SouthSide Schoo
Date: Fri 2/13/15

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

Page 1
