

SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17															
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016			Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017				
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May			
SOUTH SIDE SCHOOL																							
COMMENCEMENT								07-Feb-17, COMMENCEMENT															
SS-1880	TENT & FUMIGATE	5	100%	0	21-Jun-16 A	23-Jun-16 A		TENT & FUMIGATE															
SS-1000	NOTICE TO PROCEED	0	100%	0	29-Apr-16 A			NOTICE TO PROCEED															
SS-1830	MOLD REMEDIATION AND REMOVAL OF 1ST FLR & 2ND FLR SUB FLOOR	15	100%	0	23-May-16 A	20-Jun-16 A		MOLD REMEDIATION AND REMOVAL OF 1ST FLR & 2ND FLR SUB FLOOR															
SS-1550	MOBILIZATION	7	100%	0	12-May-16 A	23-May-16 A		MOBILIZATION															
SS-1020	LETTER TO CITY - START DATE 5/16/16	0	100%	0	16-May-16 A	16-May-16 A		LETTER TO CITY - START DATE 5/16/16															
SS-1840	DCC LETTER TO CITY - START WORK 5/16	5	100%	0	29-Apr-16 A	05-May-16 A		DCC LETTER TO CITY - START WORK 5/16															
SS-1010	ACQUIRE BUILDING PERMITS	10	95%	1	29-Apr-16 A	07-Feb-17	5	ACQUIRE BUILDING PERMITS															
SUBMITTALS								24-Apr-17															
SUBMIT								16-Mar-17, SUBMITTALS															
SS-1180	WOOD DOORS - SUBMIT	45	100%	0	02-May-16 A	06-Jan-17 A		WOOD DOORS - SUBMIT															
SS-1050	WATER SYSTEMS - SUBMIT	42	100%	0	18-Jul-16 A	22-Jul-16 A		WATER SYSTEMS - SUBMIT															
SS-1160	SEALANTS, CAULKING AND SEALS - SUBMIT	41	100%	0	07-Nov-16 A	18-Nov-16 A		SEALANTS, CAULKING AND SEALS - SUBMIT															
SS-1120	ROUGH CARPENTRY - SUBMIT	51	100%	0	02-May-16 A	27-Jan-17 A		ROUGH CARPENTRY - SUBMIT															
SS-1220	RESILIENT TILE FLOORING - SUBMIT	61	60%	24	02-May-16 A	13-Mar-17	16	RESILIENT TILE FLOORING - SUBMIT															
SS-1210	PORCELAIN/CERAMIC TILE - SUBMIT	55	94.55%	3	02-May-16 A	09-Feb-17	12	PORCELAIN/CERAMIC TILE															
SS-1270	PLUMBING FIXTURES - SUBMIT	56	100%	0	18-Jul-16 A	22-Jul-16 A		PLUMBING FIXTURES - SUBMIT															
SS-1170	METAL DOORS AND FRAMES - SUBMIT	51	100%	0	07-Oct-16 A	06-Jan-17 A		METAL DOORS AND FRAMES - SUBMIT															
SS-1070	IRRIGATION SYSTEM - SUBMIT	51	100%	0	14-Sep-16 A	15-Sep-16 A		IRRIGATION SYSTEM - SUBMIT															
SS-1280	HVAC EQUIPMENT - SUBMIT	31	100%	0	06-Jun-16 A	13-Jun-16 A		HVAC EQUIPMENT - SUBMIT															
Critical Remaining Work Remaining Work Milestone				Summary				1 BASELINE SCHEDULE								1 BASLINE SCHEDULE - BY AREA							

Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016			Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017	
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May

SOUTH SIDE SCHOOL

COMMENCEMENT

SS-1880	TENT & FUMIGATE	5	100%	0	21-Jun-16 A	23-Jun-16 A		TENT & FUMIGATE
SS-1000	NOTICE TO PROCEED	0	100%	0	29-Apr-16 A			NOTICE TO PROCEED
SS-1830	MOLD REMEDIATION AND REMOVAL OF 1ST FLR & 2ND FLR SUB FLOOR	15	100%	0	23-May-16 A	20-Jun-16 A		MOLD REMEDIATION AND REMOVAL OF 1ST FLR & 2ND FLR SUB FLOOR
SS-1550	MOBILIZATION	7	100%	0	12-May-16 A	23-May-16 A		MOBILIZATION
SS-1020	LETTER TO CITY - START DATE 5/16/16	0	100%	0	16-May-16 A	16-May-16 A		LETTER TO CITY - START DATE 5/16/16
SS-1840	DCC LETTER TO CITY - START WORK 5/16	5	100%	0	29-Apr-16 A	05-May-16 A		DCC LETTER TO CITY - START WORK 5/16
SS-1010	ACQUIRE BUILDING PERMITS	10	95%	1	29-Apr-16 A	07-Feb-17	5	ACQUIRE BUILDING PERMITS

SUBMITTALS

SUBMIT

SS-1180	WOOD DOORS - SUBMIT	45	100%	0	02-May-16 A	06-Jan-17 A		WOOD DOORS - SUBMIT
SS-1050	WATER SYSTEMS - SUBMIT	42	100%	0	18-Jul-16 A	22-Jul-16 A		WATER SYSTEMS - SUBMIT
SS-1160	SEALANTS, CAULKING AND SEALS - SUBMIT	41	100%	0	07-Nov-16 A	18-Nov-16 A		SEALANTS, CAULKING AND SEALS - SUBMIT
SS-1120	ROUGH CARPENTRY - SUBMIT	51	100%	0	02-May-16 A	27-Jan-17 A		ROUGH CARPENTRY - SUBMIT
SS-1220	RESILIENT TILE FLOORING - SUBMIT	61	60%	24	02-May-16 A	13-Mar-17	16	RESILIENT TILE FL
SS-1210	PORCELAIN/CERAMIC TILE - SUBMIT	55	94.55%	3	02-May-16 A	09-Feb-17	12	PORCELAIN/CERAMIC TILE
SS-1270	PLUMBING FIXTURES - SUBMIT	56	100%	0	18-Jul-16 A	22-Jul-16 A		PLUMBING FIXTURES - SUBMIT
SS-1170	METAL DOORS AND FRAMES - SUBMIT	51	100%	0	07-Oct-16 A	06-Jan-17 A		METAL DOORS AND FRAMES - SUB
SS-1070	IRRIGATION SYSTEM - SUBMIT	51	100%	0	14-Sep-16 A	15-Sep-16 A		IRRIGATION SYSTEM - SUBMIT
SS-1280	HVAC EQUIPMENT - SUBMIT	31	100%	0	06-Jun-16 A	13-Jun-16 A		HVAC EQUIPMENT - SUBMIT

 Critical Remaining Work  Remaining Work ◆ Milestone	 Summary	1 BASELINE SCHEDULE	1 BASLINE SCHEDULE - BY AREA
---	---	---------------------	---------------------------------

SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17												
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016			Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017	
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SS-1200	GYPSON DRYWALL SYSTEMS - SUBMIT	41	100%	0	10-Aug-16 A	12-Aug-16 A														
SS-1260	FIRE PROTECTION SYSTEM - SUBMIT	40	100%	0	28-Sep-16 A	29-Sep-16 A														
SS-1090	CONCRETE UNIT MASONRY - SUBMIT	46	100%	0	29-Apr-16 A	16-Aug-16 A														
SS-1080	CAST IN PLACE CONCRETE - SUBMIT	46	100%	0	29-Apr-16 A	01-Jul-16 A														
SS-1130	BUILDING INSULATION - SUBMIT	4	100%	0	06-Oct-16 A	12-Dec-16 A														
SS-1040	ASPHALTIC CONCRETE PAVING - SUBMIT	56	50%	28	03-Oct-16 A	16-Mar-17	24													
SS-1190	ALUMINUM WINDOWS - SUBMIT	51	100%	0	02-May-16 A	18-Nov-16 A														
APPROVE																				
SS-1440	WOOD DOORS - APPROVE	10	100%	0	06-Jan-17 A	11-Jan-17 A														
SS-1310	WATER SYSTEMS - APPROVE	10	100%	0	22-Mar-16 A	29-Aug-16 A														
SS-1420	SEALANTS, CAULKING AND SEALS - APPROVE	10	100%	0	19-Nov-16 A	22-Nov-16 A														
SS-1380	ROUGH CARPENTRY - APPROVE	10	100%	0	27-Jan-17 A	06-Feb-17 A														
SS-1480	RESILIENT TILE FLOORING - APPROVE	10	0%	10	13-Mar-17	27-Mar-17	16													
SS-1470	PORCELAIN/CERAMIC TILE - APPROVE	10	0%	10	10-Feb-17	23-Feb-17	12													
SS-1530	PLUMBING FIXTURES - APPROVE	10	100%	0	22-Jul-16 A	09-Aug-16 A														
SS-1430	METAL DOORS AND FRAMES - APPROVE	10	90%	1	06-Jan-17 A	07-Feb-17	58													
SS-1330	IRRIGATION SYSTEM - APPROVE	10	100%	0	15-Sep-16 A	19-Oct-16 A														
SS-1540	HVAC EQUIPMENT - APPROVE	10	100%	0	13-Jun-16 A	15-Jun-16 A														
SS-1460	GYPSON DRYWALL SYSTEMS - APPROVE	10	100%	0	12-Aug-16 A	23-Aug-16 A														
SS-1520	FIRE PROTECTION SYSTEM - APPROVE	10	100%	0	29-Jul-16 A	11-Aug-16 A														
Critical Remaining Work Summary Remaining Work Milestone							2 BASELINE SCHEDULE							2 BASLINE SCHEDULE - BY AREA						

SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17												
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016			Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017	
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SS-1350	CONCRETE UNIT MASONRY - APPROVE	10	100%	0	16-Aug-16 A	26-Aug-16 A														
SS-1340	CAST IN PLACE CONCRETE - APPROVE	10	100%	0	05-Jul-16 A	27-Jul-16 A														
SS-1390	BUILDING INSULATION - APPROVE	10	100%	0	12-Dec-16 A	15-Dec-16 A														
SS-1300	ASPHALTIC CONCRETE PAVING - APPROVE	10	0%	10	17-Mar-17	30-Mar-17	24													
SS-1450	ALUMINUM WINDOWS - APPROVE	10	100%	0	18-Nov-16 A	22-Nov-16 A														
DELIVER																				
SS-1710	WOOD DOORS - FAB/DEL	35	30%	25	06-Jan-17 A	13-Mar-17	27													
SS-1580	WATER SYSTEMS - FAB/DEL	20	100%	0	22-Nov-16 A	16-Dec-16 A														
SS-1690	SEALANTS, CAULKING AND SEALS - FAB/DEL	10	100%	0	23-Nov-16 A	13-Dec-16 A														
SS-1650	ROUGH CARPENTRY - FAB/DEL	5	50%	3	07-Nov-16 A	09-Feb-17	77													
SS-1750	RESILIENT TILE FLOORING - FAB/DEL	20	0%	20	27-Mar-17	24-Apr-17	16													
SS-1740	PORCELAIN/CERAMIC TILE - FAB/DEL	35	0%	35	24-Feb-17	13-Apr-17	12													
SS-1800	PLUMBING FIXTURES - FAB/DEL	15	0%	15	07-Feb-17	27-Feb-17	56													
SS-1700	METAL DOORS AND FRAMES - FAB/DEL	30	50%	15	06-Jan-17 A	28-Feb-17	58													
SS-1600	IRRIGATION SYSTEM - FAB/DEL	30	20%	24	19-Oct-16 A	10-Mar-17	43													
SS-1810	HVAC EQUIPMENT - FAB/DEL	20	100%	0	28-Nov-16 A	13-Jan-17 A														
SS-1730	GYPSUM DRYWALL SYSTEMS - FAB/DEL	5	100%	0	12-Dec-16 A	20-Dec-16 A														
SS-1790	FIRE PROTECTION SYSTEM - FAB/DEL	4	100%	0	19-Oct-16 A	14-Dec-16 A														
SS-1620	CONCRETE UNIT MASONRY - FAB/DEL	5	100%	0	07-Nov-16 A	18-Nov-16 A														
SS-1610	CAST IN PLACE CONCRETE - FAB/DEL	5	100%	0	27-Sep-16 A	06-Jan-17 A														
Critical Remaining Work				3 BASELINE SCHEDULE				3												
Remaining Work								BASLINE SCHEDULE - BY AREA												
Milestone																				

SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17												
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016		Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017		
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SS-1660	BUILDING INSULATION - FAB/DEL	5	0%	5	16-Jan-17 A	13-Feb-17	24													
SS-1570	ASPHALTIC CONCRETE PAVING - FAB/DEL	1	0%	1	31-Mar-17	31-Mar-17	24													
SS-1720	ALUMINUM WINDOWS - FAB/DEL	35	50%	18	23-Nov-16 A	02-Mar-17	57													
BLDG RENOVATION																				
CHANGES / DELAYS / DISRUPTIONS																				
PR 1 - REPLACE DOMESTIC& FIRE WATER / NEW PARAPET CAP																				
SS-3232	DCC SUBMITS RCO 3RRR - NEW DOMESTIC & FIRE WATER, NEW COPING CAP	1	100%	0	31-Aug-16 A	31-Aug-16 A														
SS-3231	CITY ISSUED PR#01 REQUESTING PROPOSAL DOMESTIC & FIRE WATER SERVICE / COPING CAP @ PARAPET WALLS	5	100%	0	20-May-16 A	20-May-16 A														
SS-3233	CITY APPROVE - RCO 3RRR CO4 - DOMESTIC & FIRE WATER SERVICE - TE - 35 Days	34	100%	0	01-Sep-16 A	05-Oct-16 A														
REPLACE PLYWOOD SUB FLOORING																				
SS-3304	RFI 90 RE LEAKING WINDOWS	5	100%	0	08-Oct-16 A	05-Jan-17 A														
SS-3242	RFI 84 RE: PR9 - ADD'L PLYWOOD REQUIRED	7	100%	0	19-Aug-16 A	26-Aug-16 A														
SS-3240	RFI 27 - EXISTING PLYWOOD GLUED DOWN / NAILING SPECIFIED	5	100%	0	31-May-16 A	07-Jun-16 A														
SS-3243	DCC - DCC SUBMIT RCO 004RR GLUE & RING SHANK NAILS	1	100%	0	31-Aug-16 A	31-Aug-16 A														
SS-3241	CITY ISSUED PR#002 - PROVIDE GLUE & RING SHANK NAILS	5	100%	0	07-Jun-16 A	07-Jun-16 A														
SS-3244	CITY APPROVE RCO 04RR - GLUE AND RING SHANK NAILS	5	100%	0	01-Sep-16 A	05-Oct-16 A														
CONDITION OF WOOD FLOORING																				
SS-3201	RFI 29 - CONDITION OF EXISTING WOOD FLOORING	7	100%	0	01-Jun-16 A	08-Jun-16 A														
Critical Remaining Work				▼ Summary				4 BASELINE SCHEDULE				4								
Remaining Work ◆ ◆ Milestone												BASLINE SCHEDULE - BY AREA								

SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17												
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016		Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017		
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SS-3204	DCC PRICING - RCO 1 - MILLING WOOD FLOORING - SUBMIT	41	100%	0	01-Sep-16 A	06-Dec-16 A														
SS-3202	CITY ISSUES PR#9 - REFURBISH SALAVAGED WOOD FLOORING	2	100%	0	09-Jun-16 A	08-Aug-16 A														
SS-3250	CITY APPROVE - RCO 1 MILLING WOOD FLOORING - APPROVE	10	100%	0	06-Dec-16 A	06-Dec-16 A														
ROOF LEAKS . REPAIRS																				
SS-3212	RFI 20 - CITY ROOFER NEEDS TO REPAIR LEAKS (NON RESPONSIVE)	5	100%	0	27-May-16 A	06-Jun-16 A														
SS-3211	RFI 15 - ROOF LEAKS / BUBBLING ROOF (NON RESPONSIVE)	2	100%	0	24-May-16 A	31-May-16 A														
SS-3222	RCO 02R - DCC PRICE & SUBMIT ROOF REPAIRS (TE 11 Days)	5	100%	0	10-Jun-16 A	27-Jun-16 A														
SS-3221	OWNER EMAIL - REQUEST PROPOSAL	5	100%	0	09-Jun-16 A	27-Jun-16 A														
SS-3223	CITY APPROVE - RCO 02R - REPAIR ROOF LEAKS - APPROVE	0	100%	0	28-Jun-16 A	28-Jun-16 A														
WINDOW CHANGES																				
SS-3256	RFI 57 - PERMIT REVISION REQUIRED - REMOVE & REINSTALL WINDOWS	9	100%	0	28-Jun-16 A	07-Jul-16 A														
SS-3251R	RFI 14R Re: LEAKING WINDOWS	5	100%	0	01-Jun-16 A	08-Jun-16 A														
SS-3251	RFI 14 - RE: LEAKING WINDOWS	7	100%	0	24-May-16 A	31-May-16 A														
SS-3258	DCC SUBMIT RCO 32 - REMOVE / REINSTALL / CAULK WINDOWS ,	45	100%	0	20-Aug-16 A	04-Oct-16 A														
SS-3253	DCC SUBMIT - RCO6 - REMOVE 3 WINDOWS	1	100%	0	27-Jun-16 A	27-Jun-16 A														
SS-3257	CITY ISSUES PR#10 - CAULK & INSTALL Windows	1	100%	0	19-Aug-16 A	19-Aug-16 A														
SS-3252	CITY EMAIL REQUESTING PROPOSAL - REMOVE (3) WINDOWS FOR INSPECTION	1	100%	0	27-Jun-16 A	27-Jun-16 A														
SS-3254	CITY APPROVE RCO6 (CO3)	1	100%	0	28-Jun-16 A	28-Jun-16 A														
CC-3259	CITY APPROVE - RCO 32	10	100%	0	05-Oct-16 A	16-Nov-16 A														
Critical Remaining Work Summary								5 BASELINE SCHEDULE				5 BASLINE SCHEDULE - BY AREA								

SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17											
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016		Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017	
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
PR12 & PR13 - ELEC SYS CHANGES & VARIOUS REVISIONS								21-Feb-17, PR12 & PR13											
SS-3400	REVISED DRAWINGS - ISSUED - PR#12 & PR#13 - ELEC SYSTEMS & VARIOUS CHANGES	5	100%	0	19-Dec-16 A	19-Dec-16 A		REVISED DRAWINGS - ISSUED - PR#12 & PR#13 - ELEC SYSTEMS & VARIOUS CHANGES											
SS-3401	DCC PRICING PR13 / RCO 45R - ELEC SYS CONDUILTS	24	100%	0	20-Dec-16 A	23-Jan-17 A		DCC PRICING PR13 / RCO 45R - ELEC SYS CONDUILTS											
SS-3402	DCC PRICING PR12 / RCO38. RCO41, RCO44, RCO49 - VARIOUS CHANGES	5	100%	0	20-Dec-16 A	27-Jan-17 A		DCC PRICING PR12 / RCO38. RCO41, RCO44, RCO49 - VARIOUS CHANGES											
SS-3404	CITY APPROVE - PR13 / RCO 45R	21	47.62%	11	24-Jan-17 A	21-Feb-17	0	CITY APPROVE - PR13 / RCO 45R											
SS-3403	CITY APPROVE - PR12	27	59.26%	11	16-Jan-17 A	21-Feb-17	0	CITY APPROVE - PR12											
TIME EXTENSIONS APPROVED - 224 CAL DAYS								22-Feb-17, TIME EXTENSIONS APPROVED - 224 CAL DAYS											
TE-006	RCO 32 - PR18 - APPROVED TIME EXTENSION 80 CAL DAY	80	100%	0	16-Nov-16 A	16-Nov-16 A		RCO 32 - PR18 - APPROVED TIME EXTENSION 80 CAL DAY											
TE-004	RCO 13R - MOISTURE TEST EXISTING ROOF - CO 4 - 2 CAL DAYS	2	100%	0	05-Oct-16 A	05-Oct-16 A		RCO 13R - MOISTURE TEST EXISTING ROOF - CO 4 - 2 CAL DAYS											
TE-003	RCO 07R TERMITE TREATMENT UNDER BLDG - CO 4 - 3 CAL DAYS	3	100%	0	05-Oct-16 A	05-Oct-16 A		RCO 07R TERMITE TREATMENT UNDER BLDG - CO 4 - 3 CAL DAYS											
TE-002	RCO 03RR - TIME EXTENSION APPROVED - CO 4 - WATER SERVICE - 35 CAL DAYS	35	100%	0	05-Oct-16 A	05-Oct-16 A		RCO 03RR - TIME EXTENSION APPROVED - CO 4 - WATER SERVICE - 35 CAL DAYS											
TE-001	RCO 02 - TIME EXTENSION APPROVED - CO 3 - ROOF LEAK REPAIRS - 11 CAL DAYS	11	100%	0	28-Jun-16 A	28-Jun-16 A		RCO 02 - TIME EXTENSION APPROVED - CO 3 - ROOF LEAK REPAIRS - 11 CAL DAYS											
TE-005	RCO - REPLACE EXISTING ROOF - CO 4 - 28 CAL DAYS	28	100%	0	05-Oct-16 A	05-Oct-16 A		RCO - REPLACE EXISTING ROOF - CO 4 - 28 CAL DAYS											
TE-007	CO6 - TIME EXTENSION - PR12, PR13 - 65 CAL DAYS	65	81.54%	12	02-Feb-17 A	22-Feb-17	103	CO6 - TIME EXTENSION - PR12, PR13 - 65 CAL DAYS											
STRUCTURE								05-Mar-17, STRUCTURE											
1ST & 2ND FLOOR								13-Feb-17, 1ST & 2ND FLOOR											
SS-1890	SELECTIVE DEMOLITION - 1ST FLR & 2ND FLR	10	100%	0	24-May-16 A	26-May-16 A		SELECTIVE DEMOLITION - 1ST FLR & 2ND FLR											
SS-1910	MEP DEMOLITION - 2ND FLR	5	100%	0	24-May-16 A	14-Jul-16 A		MEP DEMOLITION - 2ND FLR											
SS-1900	MEP DEMOLITION - 1ST FLR	10	100%	0	24-May-16 A	14-Jul-16 A		MEP DEMOLITION - 1ST FLR											
Actual Work Remaining Work Critical Remaining Work Milestone Summary				7 BASELINE SCHEDULE				7 BASLINE SCHEDULE - BY AREA											

SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17															
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016		Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017					
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May			
SS-1970	INSTALL WOOD SUB FLOOR FRAMING . DECK - 1ST FLR & 2ND FLR	5	90%	5	05-Oct-16 A	13-Feb-17	5	INSTALL WOOD SUB FLOOR FRAMING . DECK - 1ST FLR & 2ND FLR															
ROOF								ROOF LEAKS DISCOVERED															
SS-3180	ROOF LEAKS DISCOVERED	1	100%	0	28-May-16 A	28-May-16 A		REPAIR ROOF LEAKS - RCO2R/OCO3															
SS-3190	REPAIR ROOF LEAKS - RCO2R/OCO3	5	100%	0	18-Jul-16 A	27-Jul-16 A		REMOVE / INSTALL NEW GUTTERS & DS - ROOF - AREA															
SS-2190	REMOVE / INSTALL NEW GUTTERS & DS - ROOF - AREA	10	0%	10	07-Feb-17	20-Feb-17	69	RCO 26RR - NEW ROOF OVER OLD ROOF & NEW COPING CAPS															
SS-3170	RCO 26RR - NEW ROOF OVER OLD ROOF & NEW COPING CAPS	20	0%	20	07-Feb-17	06-Mar-17	9	ELEVATOR - TESTING & FINAL INSPECTIONS - 1ST FLR															
SS-3050	ELEVATOR - TESTING & FINAL INSPECTIONS - 1ST FLR	3	65%	3	12-Nov-16 A	05-May-17	25	CAULKING & SEALING - ROOF															
SS-2350	CAULKING & SEALING - ROOF	10	0%	10	21-Feb-17	06-Mar-17	69	BITUMINOUS ROOF @ CANOPIES															
SS-1990	BITUMINOUS ROOF @ CANOPIES	10	0%	10	07-Feb-17	20-Feb-17	19	WATERPROOF REAR CONC STAIRS															
EXTERIOR								WATERPROOF / REPLACE STUCCO															
SS-3230	WATERPROOF REAR CONC STAIRS	5	100%	0	27-Dec-16 A	17-Jan-17 A		STUCCO															
SS-3220	WATERPROOF / REPLACE STUCCO	5	100%	0	07-Dec-16 A	05-Jan-17 A		SELECTIVE DEMO - EXT WALLS															
SS-2250	STUCCO	10	100%	0	28-Oct-16 A	01-Nov-16 A		REINSTALL WINDOWS - RCO 32 - 1ST FLR															
SS-2030	SELECTIVE DEMO - EXT WALLS	5	100%	0	06-Sep-16 A	06-Sep-16 A		REINSTALL WINDOWS - 2ND FLR															
SS-3200	REINSTALL WINDOWS - RCO 32 - 1ST FLR	20	100%	0	21-Nov-16 A	23-Nov-16 A		RCO 32 CAULK WINDOWS- 2ND FLR															
SS-3210	REINSTALL WINDOWS - 2ND FLR	20	100%	0	21-Nov-16 A	23-Nov-16 A		RCO 32 CAULK WINDOWS- 1ST FLR															
SS-3269	RCO 32 CAULK WINDOWS- 2ND FLR	0	100%	0	16-Dec-16 A	05-Jan-17 A		PAINTING - EXTERIOR															
SS-3261	RCO 32 CAULK WINDOWS- 1ST FLR	10	100%	0	22-Nov-16 A	13-Dec-16 A		JOINT SEALANTS															
SS-2580	PAINTING - EXTERIOR	0	0%	0	21-Feb-17	21-Feb-17	76	INSTALL / WINDOWS STOREFRONT															
SS-2510	JOINT SEALANTS	5	90%	0	12-Dec-16 A	21-Feb-17	76																
SS-2390	INSTALL / WINDOWS STOREFRONT	5	0%	5	07-Feb-17	13-Feb-17	24																
Actual Work Critical Remaining Work Summary								8 BASELINE SCHEDULE								8 BASLINE SCHEDULE - BY AREA							
Remaining Work Milestone																							

SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17												
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016		Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017		
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SS-2240	F/R/P CONC WEST SIDE STAIRS	8	100%	0	26-Oct-16 A	11-Jan-17 A														
SS-2360	F/R/P CONC WEST SIDE HC RAMP	5	100%	0	26-Oct-16 A	11-Jan-17 A														
SS-2150	EXT STUDS ./ BLOCKING	5	100%	0	27-Oct-16 A	01-Nov-16 A														
SS-2460	ELEC - EXT LIGHT FIXTURES	5	45%	5	22-Nov-16 A	20-Feb-17	76													
SS-1920	DEMO EXTERIOR FOR WEST SIDE STAIRS	5	100%	0	16-Sep-16 A	20-Sep-16 A														
SS-2070	DEMO - MODIFY EXISTING OPENINGS	10	100%	0	06-Sep-16 A	06-Sep-16 A														
SS-2020	CONC FOUNDATIONS @ WEST SIDE STAIRS	6	100%	0	04-Oct-16 A	26-Oct-16 A														
SS-2140	CMU WALLS @ W SIDE STAIRS	5	100%	0	06-Dec-16 A	09-Dec-16 A														
SS-2620	ALUM HANDRAILS	3	0%	3	16-Mar-17	20-Mar-17	59													
ROUGH IN																				
1ST FLOOR																				
SS-2130	WOOD STAIRS - 1ST FLR	10	0%	10	23-Feb-17	09-Mar-17	7													
SS-2110	SET HM FRAMES - 1ST FLR	5	0%	5	23-Feb-17	02-Mar-17	16													
SS-1930.2	REVISED CEILING FRAMING -1ST FLR	5	0%	5	23-Feb-17	02-Mar-17	6													
SS-3360	REPLACE EXISTING FLOOR RCO 4RR - 1ST FLR	5	0%	5	07-Feb-17	13-Feb-17	1													
SS-2420	MEP ROUGH INSPECTIONS - 1ST FLR	3	50%	2	06-Dec-16 A	15-Mar-17	1													
SS-2080,1	INSTALL SHOWER PANS - 1ST FLOOR	1	0%	1	07-Feb-17	07-Feb-17	27													
SS-2230.4	INSTALL SECURITY CONDUITS ROUGH - 1ST FLOOR	14	0%	14	23-Feb-17	14-Mar-17	1													
SS-2230.7	INSTALL REVISED INTERCOM CONDUITS ROUGH - 1ST FLOOR	5	0%	5	23-Feb-17	01-Mar-17	10													
SS-2017.11	INSTALL REVISED DATA CONDUITS ROUGH TO NEW IT ROOM - 1ST FLOOR	5	0%	5	07-Feb-17	13-Feb-17	22													
Actual Work Remaining Work				Critical Remaining Work Milestone				9 BASELINE SCHEDULE				9 BASLINE SCHEDULE - BY AREA								


SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17												
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016			Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017	
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
10	SS-2230.6	INSTALL REVISED DATA CONDUITS ROUGH TO NEW IT ROOM - 1ST FLOOR	14	0%	14	23-Feb-17	14-Mar-17	10											INSTALL REVISED DATA CONDUITS ROUGH TO NEW IT ROOM - 1ST FLOOR	
	SS-2230.1	INSTALL REVISED CCTV CONDUITS ROUGH - 1ST FLOOR	14	0%	14	22-Feb-17	13-Mar-17	0											INSTALL REVISED CCTV CONDUITS ROUGH - 1ST FLOOR	
	SS-2230.3	INSTALL REVISED CATV CONDUITS ROUGH - 1ST FLOOR	14	0%	14	23-Feb-17	14-Mar-17	1											INSTALL REVISED CATV CONDUITS ROUGH - 1ST FLOOR	
	SS-2300	INSTALL PLUMBING INSULATION - 1ST FLR	3	50%	3	12-Dec-16 A	07-Mar-17	12											INSTALL PLUMBING INSULATION - 1ST FLR	
	SS-2080	INSTALL PLUMB R-I - WALLS - 1ST FLR	12	100%	0	15-Aug-16 A	19-Dec-16 A												INSTALL PLUMB R-I - WALLS - 1ST FLR	
	SS-1930	INSTALL INT METAL FRAMING - 1ST FLR	10	25%	8	24-Jan-17 A	23-Feb-17	1											INSTALL INT METAL FRAMING - 1ST FLR	
	SS-2160	INSTALL HVAC EQUIP PIPING - 1ST FLR	17	95%	1	04-Oct-16 A	01-Mar-17	10											INSTALL HVAC EQUIP PIPING - 1ST FLR	
	SS-2040	INSTALL HVAC EQUIP - 1ST FLR	15	70%	5	06-Dec-16 A	06-Mar-17	10											INSTALL HVAC EQUIP - 1ST FLR	
	SS-2060	INSTALL FIRE SPRKLR R-I - 1ST FLR	12	100%	0	26-Oct-16 A	08-Nov-16 A												INSTALL FIRE SPRKLR R-I - 1ST FLR	
	SS-2000	INSTALL ELEC ROUGH - WALLS - 1ST FLR	12	60%	5	11-Aug-16 A	20-Feb-17	1											INSTALL ELEC ROUGH - WALLS - 1ST FLR	
	SS-2010	INSTALL DUCTWORK - 1ST FLR	12	90%	1	12-Jul-16 A	20-Feb-17	10											INSTALL DUCTWORK - 1ST FLR	
	SS-2230.2	INSTALL CCTV CONDUITS TO POLE - WEST PARKING LOT	3	100%	0	19-Dec-16 A	21-Dec-16 A												INSTALL CCTV CONDUITS TO POLE - WEST PARKING LOT	
	SS-2230.5	INSTALL CARD ACCESS SYS CONDUIT ROUGH - 1ST FLOOR	14	0%	14	23-Feb-17	14-Mar-17	10											INSTALL CARD ACCESS SYS CONDUIT ROUGH - 1ST FLOOR	
	SS-2320	INSTALL BLDG INSULATION - 1ST FLR	5	25%	4	16-Jan-17 A	08-Mar-17	12											INSTALL BLDG INSULATION - 1ST FLR	
	SS-1930.4	INSTALL / MODIFY STRUCTURAL FRAMING FOR SHOWERS	2	100%	0	11-Jan-17 A	12-Jan-17 A												INSTALL / MODIFY STRUCTURAL FRAMING FOR SHOWERS	
	SS-2450	FRAMING INSPECTION - 1ST FLOOR	1	0%	1	16-Mar-17	16-Mar-17	1											FRAMING INSPECTION - 1ST FLOOR	
	SS-1930.3	FRAME / BOX OUT RECESS FOR NEW AC CEILING CASSETTES - 1ST FLOOR	5	0%	5	02-Mar-17	09-Mar-17	6											FRAME / BOX OUT RECESS FOR NEW AC CEILING CASSETTES - 1ST FLOOR	
	SS-2230	ELEC F/A & SYSTEMS ROUGH - 1ST FLR	10	80%	2	11-Aug-16 A	22-Feb-17	1											ELEC F/A & SYSTEMS ROUGH - 1ST FLR	
SS-2590	ELEC - POWER FOR ELEV	5	0%	5	31-Mar-17	06-Apr-17	25											ELEC - POWER FOR ELEV		
Actual Work Remaining Work Critical Remaining Work Milestone Summary				10 BASELINE SCHEDULE				10 BASLINE SCHEDULE - BY AREA												

SOUTH SIDE SCHOOL				DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17												
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016		Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017		
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SS-3360.1	ADD 2ND LAYER 3/4" PLYWOOD FLOORING - 1ST FLOOR - ROOM 106,112 & 113	1	0%	1	14-Feb-17	14-Feb-17	73													
2ND FLOOR								03-Apr-17, 2ND FLOOR												
SS-2310	SET WOOD FRAMES - 2ND FLR	5	0%	5	28-Feb-17	07-Mar-17	23													
SS-2120.2	REVISED CEILING FRAMING - 2ND FLR	5	0%	5	28-Feb-17	07-Mar-17	10													
SS-3270	REPLACE EXISTING FLOOR RCO 1 & 4R - 2ND FLR	10	100%	0	05-Oct-16 A	14-Oct-16 A														
SS-2120.4	REMOVE & CLOSE UP 2 EXISTING ROOF CURBS	10	0%	10	07-Feb-17	20-Feb-17	15													
SS-2400	MEP ROUGH INSPECTIONS - 2ND FLR	3	40%	2	09-Dec-16 A	30-Mar-17	0													
SS-2120.5	INSTALL STRUCTURAL FRAMING FOR KEF-1 CURB	10	0%	10	07-Feb-17	20-Feb-17	15													
SS-2330.4	INSTALL SECURITY CONDUITS ROUGH - 2ND FLOOR	14	0%	14	15-Mar-17	03-Apr-17	75													
SS-2330.6	INSTALL REVISED DATA CONDUITS ROUGH TO NEW IT - ROOM 2ND FLOOR	5	0%	5	15-Mar-17	21-Mar-17	84													
SS-2220.1	INSTALL REVISED CCTV CONDUITS ROUGH - 2ND FLOOR	14	0%	14	10-Mar-17	29-Mar-17	0													
SS-2120.3	INSTALL PLYWOOD ON IT WALLS - 2ND FLOOR	5	0%	5	10-Mar-17	17-Mar-17	23													
SS-2280	INSTALL PLUMBING INSULATION - 2ND FLR	10	0%	10	28-Feb-17	13-Mar-17	35													
SS-2170	INSTALL PLUMB R-I - WALLS - 2ND FLR	10	75%	3	24-Aug-16 A	27-Feb-17	21													
SS-2200	INSTALL PLUMB R-I - CLGS - 2ND FLR	10	25%	8	23-Jan-17 A	06-Mar-17	31													
SS-2120.6	INSTALL NEW ROOF CURB FOR KEF-1	2	0%	2	21-Feb-17	22-Feb-17	103													
SS-2170.1	INSTALL NEW CONDENSATE FOR IT - ROOM 209 AC UNIT	1	0%	1	02-Mar-17	03-Mar-17	19													
SS-2120	INSTALL INT METAL FRAMING - 2ND FLR	10	70%	3	18-Oct-16 A	28-Feb-17	6													
SS-2370	INSTALL HVAC EQUIP PIPING - 2ND FLR	10	100%	0	04-Oct-16 A	19-Dec-16 A														
Actual Work Remaining Work Critical Remaining Work Milestone Summary				11 BASELINE SCHEDULE				11 BASLINE SCHEDULE - BY AREA												

SOUTH SIDE SCHOOL					DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17														
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016		Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017					
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May			
SS-2270	INSTALL HVAC EQUIP - 2ND FLR -	5	70%	2	06-Jan-17 A	10-Mar-17	17											INSTALL HVAC EQUIP - 2ND FLR -					
SS-2260	INSTALL FIRE SPRKLR R-I - 2ND FLR	10	100%	0	26-Oct-16 A	09-Dec-16 A												INSTALL FIRE SPRKLR R-I - 2ND FLR					
SS-2220	INSTALL ELECT ROUGH - OH - 2ND FLR	10	80%	2	02-Sep-16 A	27-Feb-17	37											INSTALL ELECT ROUGH - OH - 2ND FLR					
SS-2180	INSTALL ELEC ROUGH - WALLS - 2ND FLR	10	80%	5	29-Aug-16 A	02-Mar-17	6											INSTALL ELEC ROUGH - WALLS - 2ND FLR					
SS-2210	INSTALL DUCTWORK - 2ND FLR	10	90%	1	09-Sep-16 A	24-Feb-17	17											INSTALL DUCTWORK - 2ND FLR					
SS-2330.5	INSTALL CARD ACCESS SYS CONDUIT ROUGH - 2ND FLOOR	14	0%	14	15-Mar-17	03-Apr-17	75											INSTALL CARD ACCESS SYS CONDUIT ROUGH - 2ND FLOOR					
SS-2340	INSTALL BLDG INSULATION - 2ND FLR	5	0%	5	02-Mar-17	09-Mar-17	19											INSTALL BLDG INSULATION - 2ND FLR					
SS-2330.3	INSTALL REVISED CATV CONDUITS ROUGH - 2ND FLOOR	14	0%	14	15-Mar-17	03-Apr-17	75											INSTALL REVISED CATV CONDUITS ROUGH - 2ND FLOOR					
SS-2430	FRAMING INSPECTION - 2ND FLR	1	0%	1	31-Mar-17	31-Mar-17	0											FRAMING INSPECTION - 2ND FLR					
SS-2120.1	FRAME NEW IT - ROOM - 2ND FLOOR	2	0%	2	08-Mar-17	10-Mar-17	10											FRAME NEW IT - ROOM - 2ND FLOOR					
SS-2017.13	FRAME / BOX OUT RECESS FOR NEW AC CEILING CASSETTES - 2ND FLOOR	5	0%	5	10-Mar-17	17-Mar-17	10											FRAME / BOX OUT RECESS FOR NEW AC CEILING CASSETTES - 2ND FLOOR					
SS-2330	ELEC F/A & SYSTEMS ROUGH - 2ND FLR	10	85%	5	02-Sep-16 A	09-Mar-17	6											ELEC F/A & SYSTEMS ROUGH - 2ND FLR					
SS-3270.1	ADD 2ND LAYER 3/4" PLYWOOD FLOORING - 2ND FLOOR - ROOM 209	1	0%	1	07-Mar-17	08-Mar-17	10											ADD 2ND LAYER 3/4" PLYWOOD FLOORING - 2ND FLOOR - ROOM 209					
FINISHES																							
2ND FLOOR																							
SS-2610	SCREW INSPECTION - 2ND FLR	1	0%	1	10-Apr-17	10-Apr-17	3											SCREW INSPECTION - 2ND FLR					
SS-2480	PLASTER RESTORATION - 2ND FLR	8	0%	8	14-Mar-17	23-Mar-17	35											PLASTER RESTORATION - 2ND FLR					
SS-2900	PAINTING TOUCH UP - 2ND FLR	5	0%	5	15-May-17	19-May-17	15											PAINTING TOUCH UP - 2ND FLR					
SS-2680	PAINT INTERIOR PRIME COAT - 2ND FLR	6	0%	6	19-Apr-17	26-Apr-17	0											PAINT INTERIOR PRIME COAT - 2ND FLR					
SS-2720	PAINT INTERIOR FINISH COAT - 2ND FLR	10	0%	10	24-Apr-17	05-May-17	0											PAINT INTERIOR FINISH COAT - 2ND FLR					
Actual Work				Critical Remaining Work				Summary															
Remaining Work				Milestone																			
12 BASELINE SCHEDULE								12 BASLINE SCHEDULE - BY AREA															

SOUTH SIDE SCHOOL					DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17											
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016			Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017	
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
SS-3000	INSTALL TOILET PARTITIONS - 2ND FLR	4	0%	4	31-May-17	05-Jun-17	0													
SS-3040	INSTALL TOILET ACCESSORIES - 2ND FLR	4	0%	4	06-Jun-17	09-Jun-17	0													
SS-2890	INSTALL RESILIENT FLOORING - 2ND FLR	7	0%	7	15-May-17	23-May-17	0													
SS-2950	INSTALL PLUMB TRIM - 2ND FLR	10	0%	10	22-May-17	02-Jun-17	5													
SS-2930	INSTALL PLUMB FIXTURES - 2ND FLR	10	0%	10	17-May-17	30-May-17	0													
SS-2810	INSTALL HVAC GRILLS/TRIM - 2ND FLR	10	0%	10	08-May-17	19-May-17	0													
SS-2820	INSTALL FIRE SPRKLR HEADS/TRIM - 2ND FLR	10	0%	10	08-May-17	19-May-17	15													
SS-2840	INSTALL FIRE EXTINGUISHERS - 2ND FLR	5	0%	5	08-May-17	12-May-17	20													
SS-2830	INSTALL FINISH HARDWARE - 2ND FLR	10	0%	10	08-May-17	19-May-17	15													
SS-2540	INSTALL ELEC FIXTURES - 2ND FLR	10	0%	10	20-Mar-17	31-Mar-17	35													
SS-2750	INSTALL ARCH WOODWORK - 2ND FLR	10	0%	10	27-Apr-17	10-May-17	17													
SS-2850	INSTALL / REFINISH WOOD FLOORING - RCO 01 - 2ND FLR	5	0%	5	08-May-17	12-May-17	15													
SS-2570	HANG DRYWALL - 2ND FLR	12	0%	12	03-Apr-17	18-Apr-17	0													
SS-2740	HANG DOORS - 2ND FLR	7	0%	7	27-Apr-17	05-May-17	15													
SS-2660	FINISH DRYWALL - 2ND FLR	12	0%	12	13-Apr-17	28-Apr-17	0													
SS-3070	CLEAN & PRELIM PUNCH - 2ND FLR	10	0%	10	12-Jun-17	23-Jun-17	0													
SS-2770	CERAMIC TILE @ BATHROOMS - 2ND FLR	12	0%	12	01-May-17	16-May-17	0													
SS-2017.14	ADD 2ND LAYER SHEETROCK TO CEILING - ROOM 204	5	0%	5	19-Apr-17	25-Apr-17	3													
1ST FLOOR																				
SS-2530	SCREW INSPECTION - 1ST FLR	1	0%	1	24-Mar-17	24-Mar-17	1													
SS-2410	PLASTER RESTORATION - 1ST FLR	8	0%	8	07-Mar-17	17-Mar-17	41													
SS-3030	PAINTING TOUCH UP - 1ST FLR	5	0%	5	02-Jun-17	08-Jun-17	1													
SS-2650	PAINT INTERIOR PRIME COAT - 1ST FLR	5	0%	5	11-Apr-17	17-Apr-17	1													
Actual Work Remaining Work				Critical Remaining Work ◆ Milestone				13 BASELINE SCHEDULE				13 BASLINE SCHEDULE - BY AREA								

SOUTH SIDE SCHOOL					DD 07-Feb-17 Dipompeo Construction Corp				08-Feb-17												
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016			Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017		
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	
	SS-2730	PAINT INTERIOR FINISH COAT - 1ST FLR	10	0%	10	24-Apr-17	05-May-17	1												PAINT	
	SS-3010	INSTALL TOILET PARTITIONS - 1ST FLR	5	0%	5	31-May-17	06-Jun-17	1													
	SS-3020	INSTALL TOILET ACCESSORIES - 1ST FLR	5	0%	5	02-Jun-17	08-Jun-17	1													
	SS-2920	INSTALL RESILIENT FLOORING - 1ST FLR	7	0%	7	15-May-17	23-May-17	1													I
	SS-2960	INSTALL PLUMB TRIM - 1ST FLR	10	0%	10	19-May-17	01-Jun-17	6													
	SS-2940	INSTALL PLUMB FIXTURES - 1ST FLR	10	0%	10	17-May-17	30-May-17	1													
	SS-2860	INSTALL HVAC GRILLS/TRIM - 1ST FLR	10	0%	10	08-May-17	19-May-17	1													IN
	SS-2880	INSTALL FIRE SPRKLR HEADS/TRIM - 1ST FLR	10	0%	10	08-May-17	19-May-17	15													IN
	SS-2990	INSTALL FIRE EXTINGUISHERS - 1ST FLR	5	0%	5	22-May-17	26-May-17	10													
	SS-2760	INSTALL FINISH HARDWARE - 1ST FLR	10	0%	10	02-May-17	15-May-17	19													INS
	SS-2870	INSTALL ELEC FIXTURES - 1ST FLR	10	0%	10	08-May-17	19-May-17	1													IN
	SS-2970	INSTALL ELEC / FA / COMM TRIM - 1ST FLR	10	0%	10	22-May-17	02-Jun-17	5													
	SS-2710	INSTALL ARCH WOODWORK - 1ST FLR	10	0%	10	18-Apr-17	01-May-17	29													INSTA
	SS-2690	INSTALL ALUM DOORS / STOREFRONT - 1ST FLR	5	0%	5	18-Apr-17	24-Apr-17	24													INSTALL
	SS-2980	INSTALL / REFINISH WOOD FLOORING - RCO 1 - 1ST FLOOR	10	0%	10	22-May-17	02-Jun-17	1													
	SS-2050	INSTALL DOOR FRAMES - 1ST FLR	5	0%	5	17-Feb-17	24-Feb-17	16													INSTALL DOOR FRAME
	SS-2470	HANG DRYWALL - 1ST FLR	12	0%	12	17-Mar-17	03-Apr-17	1													HANG DRYW
	SS-2700	HANG DOORS - 1ST FLR	7	0%	7	18-Apr-17	26-Apr-17	1													HANG D
	SS-2520	FINISH DRYWALL - 1ST FLR	12	0%	12	24-Mar-17	10-Apr-17	1													FINISH DRY
	SS-3060	CLEAN & PRELIM PUNCH - 1ST FLR	10	0%	10	09-Jun-17	22-Jun-17	1													
SS-2640	CERAMIC TILE @ BATHROOMS - 1ST FLR	12	0%	12	14-Apr-17	01-May-17	12													CERA	
Actual Work Remaining Work					Critical Remaining Work Milestone					14 BASELINE SCHEDULE					14 BASLINE SCHEDULE - BY AREA						

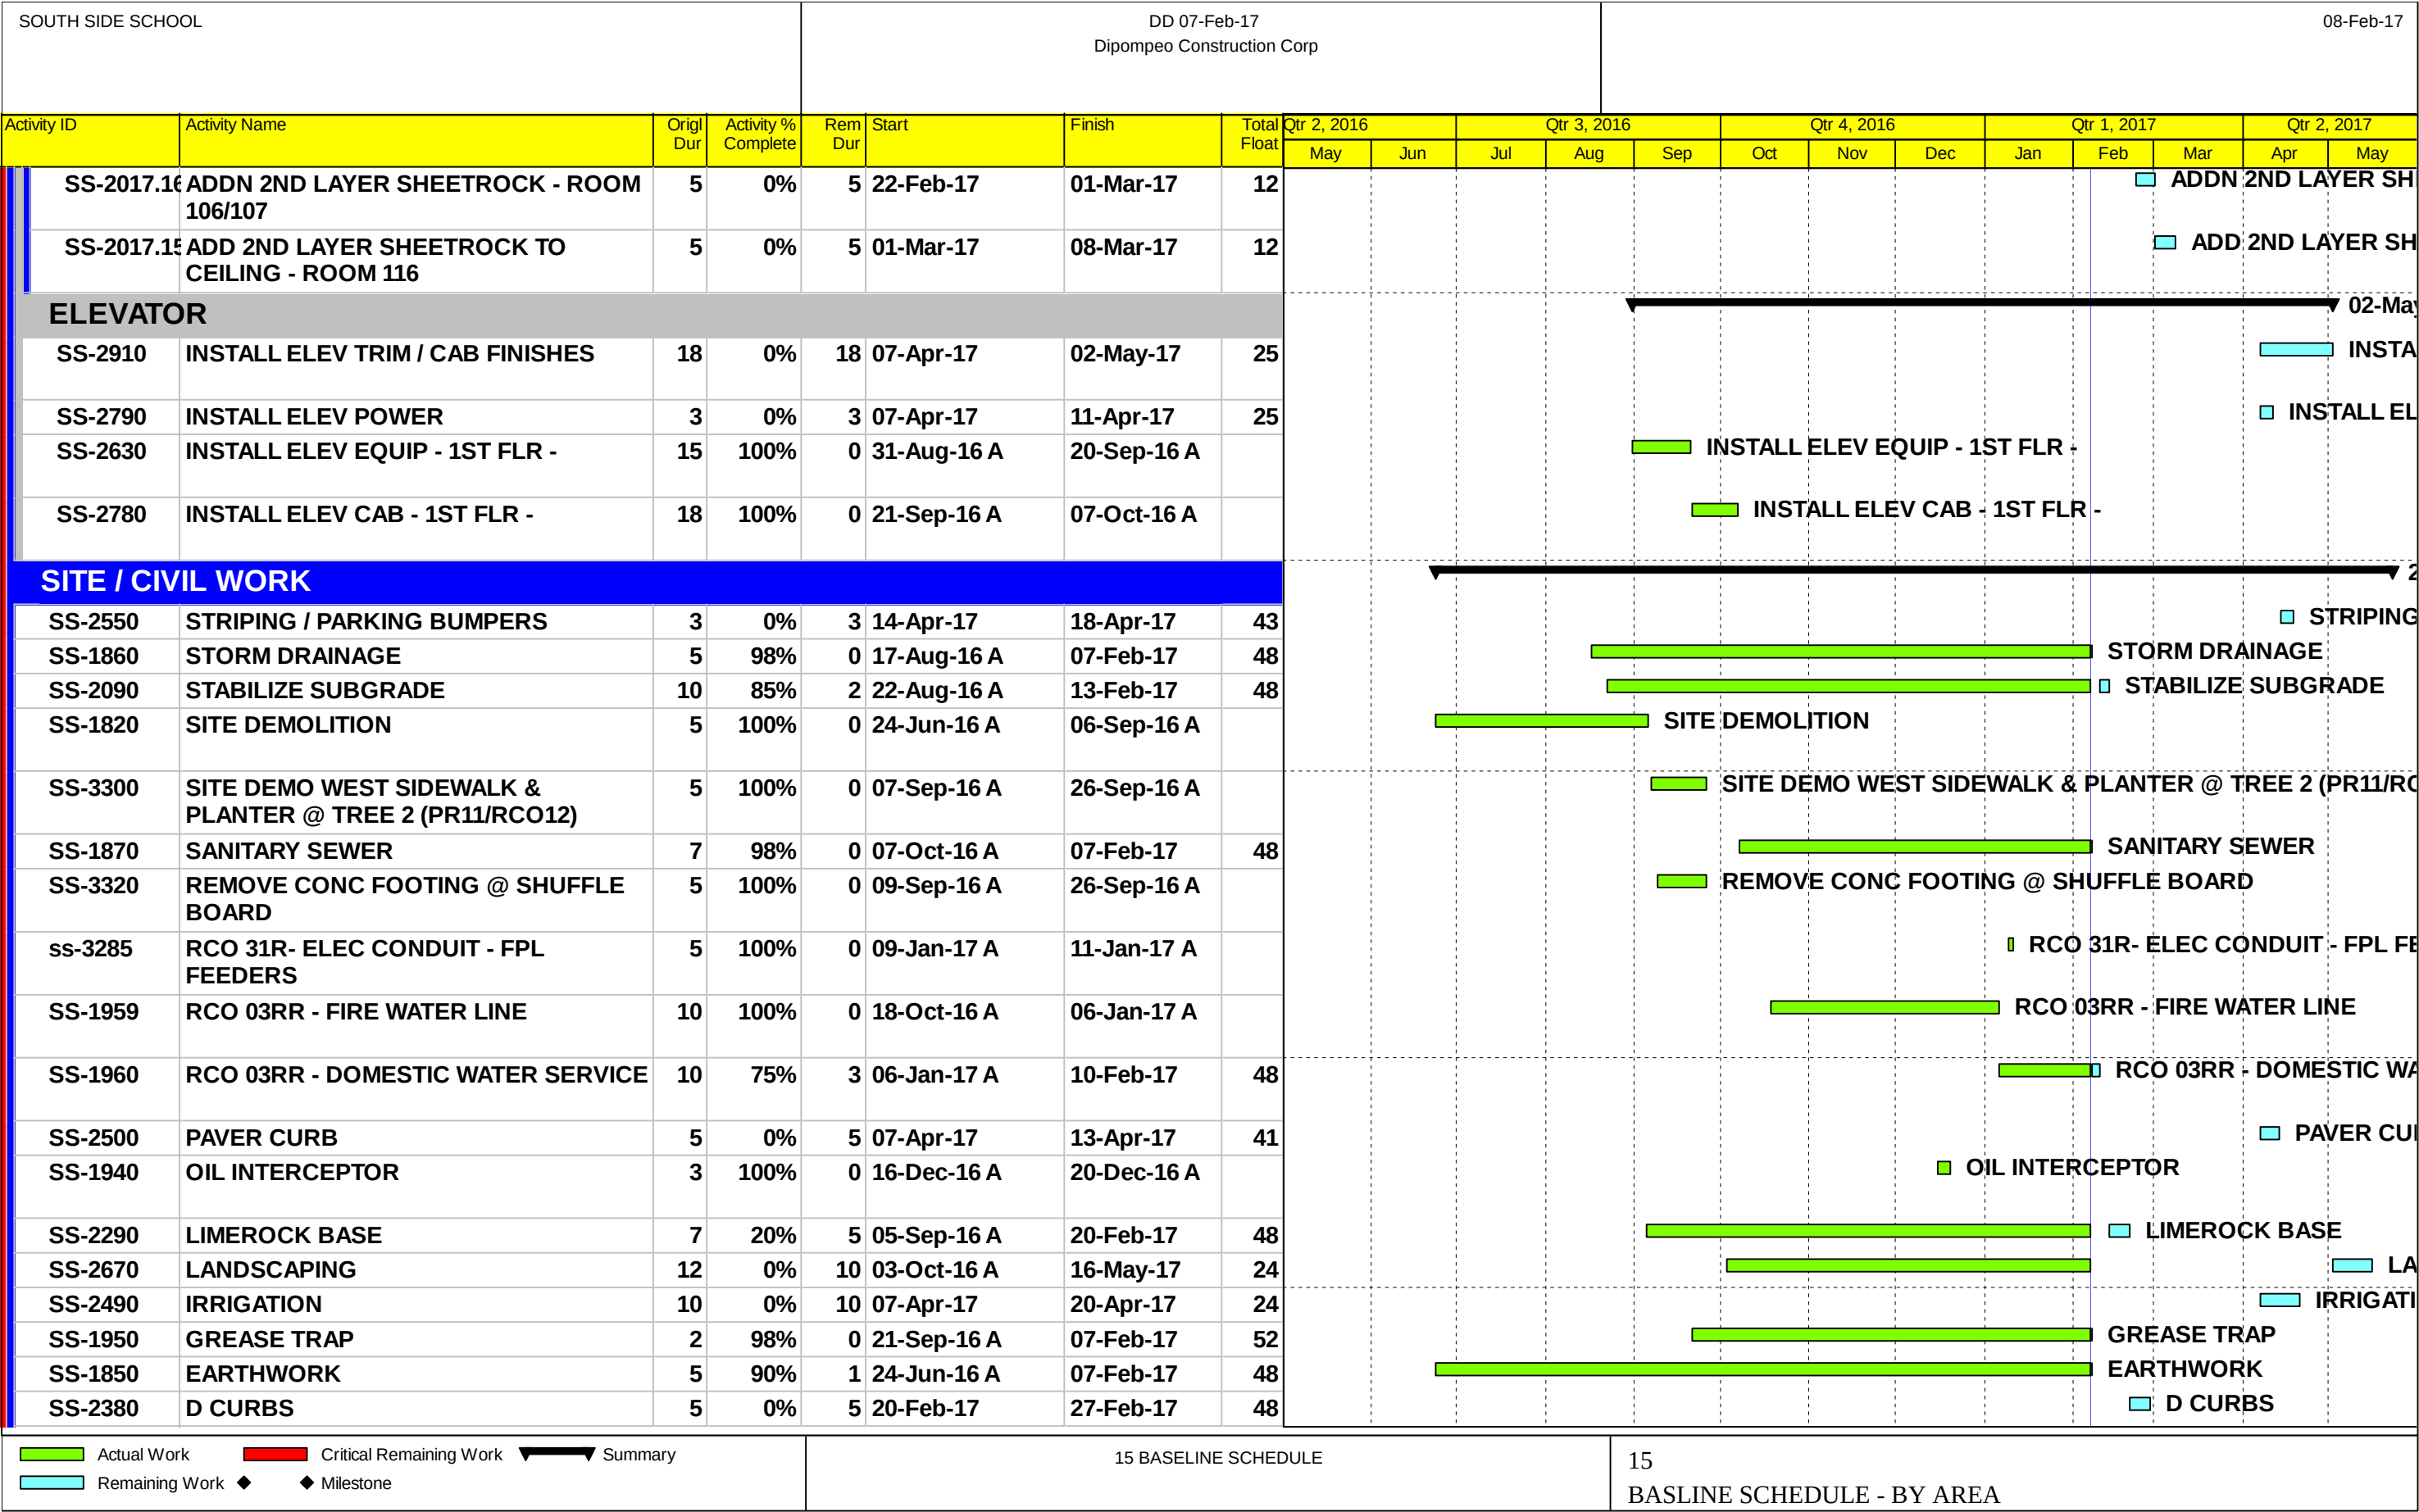

SOUTH SIDE SCHOOL					DD 07-Feb-17 Dipompeo Construction Corp					08-Feb-17															
Activity ID	Activity Name	Origl Dur	Activity % Complete	Rem Dur	Start	Finish	Total Float	Qtr 2, 2016		Qtr 3, 2016			Qtr 4, 2016			Qtr 1, 2017			Qtr 2, 2017						
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May					
SS-2600	CONCRETE SIDEWALKS	7	0%	7	21-Apr-17	01-May-17	24													CONC					
SS-2560	CONCRETE PAVERS	5	0%	5	14-Apr-17	20-Apr-17	41													CONCRE					
SS-2800	CLEANUP & PRELIMINARY PUNCH	5	0%	5	16-May-17	23-May-17	24													C					
SS-2440	ASPHALT PAVING	4	0%	4	03-Apr-17	06-Apr-17	24													ASPHALT PA					
COMPLETION																									
SS-3090	MILESTONE - SUBSTANTIAL COMPLETION	0	0%	0		26-Jun-17*	0																		
SS-3110	MILESTONE - FINAL COMPLETION	0	0%	0		17-Jul-17*	0																		
SS-3100	COMPETE A/E PUCH LIST & CLOSEOUT	15	0%	15	27-Jun-17	17-Jul-17	0																		
SS-4600	ADJUSTED CONTRACT COMPLETION DATE (W 224 DAY TE)	0	0%	0		17-Jul-17*	0																		
SS-3080	A/E INSPECTION	1	0%	1	26-Jun-17	26-Jun-17	0																		
Actual Work Remaining Work					Critical Remaining Work ◆ Milestone					Summary					16 BASELINE SCHEDULE						16 BASLINE SCHEDULE - BY AREA				
